




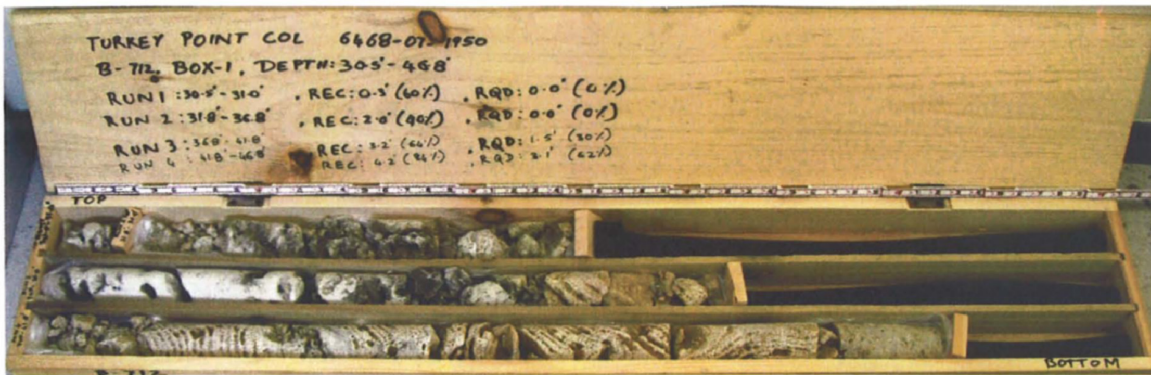

B-712 - Box 1

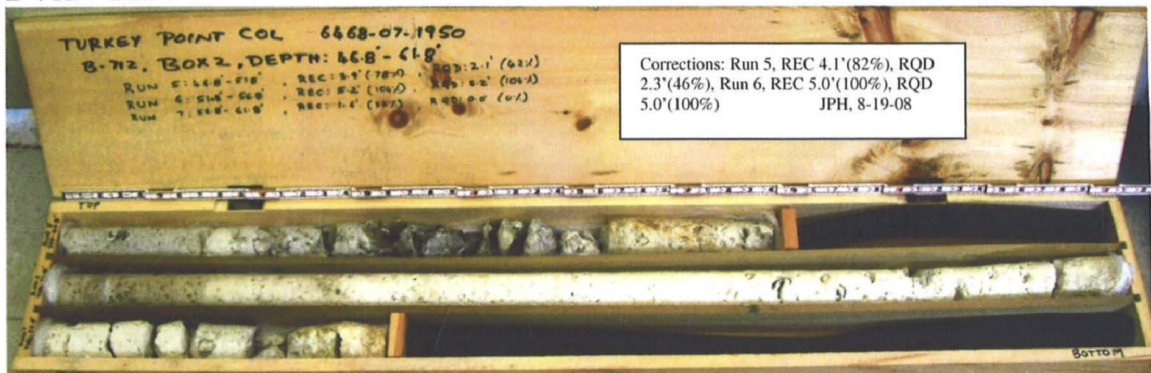

B-712 - Box 2

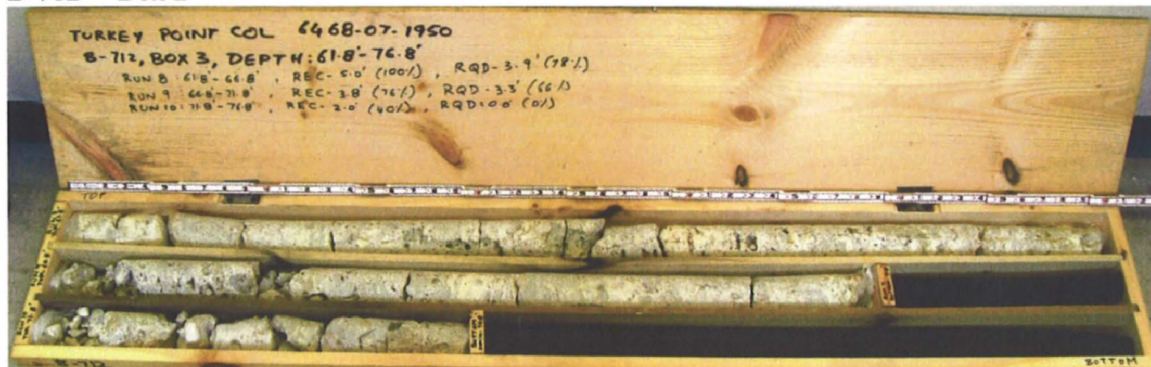

B-712 - Box 3



B-712 - Box 4



B-712 - Box 5



GEOTECHNICAL BORING LOG

Prepared By 2022 Date 5-30-08Checked By HTM Date 5-30-08

SHEET 1 OF 3

BECHTEL PROJECT NO.: 25409					MACTEC PROJECT NO.: 6468-07-1950					COUNTY: Miami-Dade		GEOLOGIST: O. Rodriguez/G. Pillappa			
SITE DESCRIPTION: Turkey Point COL					DRILL MACHINE: CME-550 (ATL)					DRILLER: L. Carter/ J. Landeros				GROUND WATER (ft)	
BORING NO.: B-713					DRILL METHOD: Mud Rotary/ Core					SAMPLE METHODS: SPT/Core				0 HR. NA	
GROUND ELEV.: -1.1 ft (NAVD88)					NORTHING: 397,179 US ft (NAD83/90)					EASTING: 875,959 US ft (NAD83/90)				24 HR. NA	
TOTAL DEPTH: 152.5 ft			BORING DIAMETER: 4" to 31.0', 3" to 152.5'					CASING DEPTH: 4" to 31.0', 3" to 118.4'				HAMMER (ID): 140 lb. Auto (MEC-03)			
DATE STARTED: 4/15/08			COMPLETED: 4/19/08			CORE SIZE: HQ3			BITS USED: 2 15/16" Roller Cone						
ELEV. (ft)	DEPTH (ft)	BLOW COUNT			BLOWS PER FOOT					SAMP. NO.	▼ MOI	L O G	SOIL AND ROCK DESCRIPTION		
		0.5ft	0.5ft	0.5ft	0	20	40	60	80	100					
-1.1					Ground Surface										
-1.1	0.0	WOH	WOH	WOH	0						713-1		-1.1	0.0	
-4.1	3.0				0						713-2		-3.6	2.5	
-6.1	5.0	31	37	30							713-3				
-8.6	7.5	7	8	7	15						713-4				
-11.1	10.0	9	20	11	31						713-5				
-13.6	12.5	5	15	11	26						713-6				
-16.1	15.0	11	7	15	22						713-7				
-20.6	19.5	7	20	50/0.4						70/0.9	713-8				
		4	5	5	10						713-9				
-25.8	24.7	3	2	WOH	2						713-10		-25.1	24.0	
		10	44	50/0.5						94/1.0	RUN-1				
-30.7	29.6										RUN-2				
-32.2	31.1										RUN-3				
-34.3	33.2										RUN-4				
-39.3	38.2										RUN-5		-49.6	48.5	
-44.3	43.2										RUN-6				
-49.3	48.2										RUN-7				
-54.3	53.2										RUN-8				
-59.3	58.2										RUN-9				
-64.3	63.2										RUN-10				
-69.3	68.2														
-74.3	73.2														

TURKEY POINT COL BORE TURKEY POINT GPJ TURKEY POINT COL GDI 5'30'08
