

NORTH ANNA 3 BORE NORTH ANNA 3 PROJECT.GPJ NORTH ANNA 3.GDT 12/4/09

BECHTEL PROJECT NO.: 25161				MACTEC PROJECT NO.: 6468-09-2473				COUNTY: Louisa, VA				GEOLOGIST: R. Clark			
SITE DESCRIPTION: North Anna 3 Project Supplement 2								DRILLER: T. Hahn/R. Hall				FLUID LEVEL (ft)			
BORING NO.: M-30 (DH)				DRILL METHOD: Mud Rotary/Rock Core				DRILL MACHINE: CME-55 Track (RAL)				0 HR. NA			
GROUND ELEV.: 313.3 ft (NAVD88)				NORTHING: 3,909,695 US ft (NAD83)				EASTING: 11,685,382 US ft (NAD83)				24 HR. 25.4			
TOTAL DEPTH: 201.7 ft				SAMPLE METHODS: ASTM D 1586-08a; 2488-09a; 2113-08; 6032-08				ROD TYPE: AWJ				HAMMER (ID): 140-lb. Auto (MEC-21)			
DATE STARTED: 9/1/09				COMPLETED: 9/9/09				HOLE DIA.: 4"				CASING DEPTH: 42.2 ft			
								CORE SIZE: HQ3				BITS USED: 3-7/8" Tri-Cone			
ELEV.	DEPTH	BLOW COUNT			BLOWS PER FOOT					SAMP.	LOG	SOIL AND ROCK DESCRIPTION			
(ft)	(ft)	0.5ft	0.5ft	0.5ft	0	20	40	60	80	100					NO.
163.7					Continued from previous page										
												HARD ROCK: Light gray, with trace pink and white, locally with orange staining, very slightly weathered to fresh, close to wide fracturing, hard to very hard, BIOTITE QUARTZ GNEISS with trace magnetite (continued)			
										RS-9					
										RS-10					
												111.6			
												201.7			
												Boring and coring terminated at 201.7 feet.			
												Boring closed by tremie method with cement-bentonite grout.			
												24 hour water level measured on 9/09/2009 prior to drilling. Borehole was at a depth of 171.5 feet.			

NORTH ANNA 3 BORE NORTH ANNA 3 PROJECT.GPJ NORTH ANNA 3.GDT 12/4/09



SHEET 1 OF 3

BECHTEL PROJECT NO.: 25161	MACTEC PROJECT NO.: 6468-09-2473	COUNTY: Louisa, VA	GEOLOGIST: R. Clark
SITE DESCRIPTION: North Anna 3 Project Supplement 2		DRILLER: T. Hahn/R. Hall	FLUID LEVEL (ft)
BORING NO.: M-30 (DH)	DRILL METHOD: Mud Rotary/Rock Core	DRILL MACHINE: CME-55 Track (RAL)	0 HR. NA
GROUND ELEV.: 313.3 ft (NAVD88)	NORTHING: 3,909,695 US ft (NAD83)	EASTING: 11,685,382 US ft (NAD83)	24 HR. 25.4
TOTAL DEPTH: 201.7 ft	SAMPLE METHODS: ASTM D 1586-08a; 2488-09a; 2113-08; 6032-08		HAMMER (ID): 140-lb. Auto (MEC-21)
DATE STARTED: 9/1/09	COMPLETED: 9/9/09	CASING DEPTH: 42.2 ft	CORE BARREL TYPE: Wireline HQ3 Triple Tube, series 6 & 10 bits

ELEV. (ft)	DEPTH (ft)	RUN (ft)	DRILL RATE (Min/ft)	REC. (ft) %	RQD (ft) %	SAMP. NO.	REC. (ft) %	RQD (ft) %	LOG	DESCRIPTION AND REMARKS
										Begin Coring @ 43.7 ft
269.6	43.7	3.0	N=50/0.0 2:01	(3.0) 100%	(1.9) 63%	RUN 1	(3.0) 100%	(1.9) 63%		269.6 HARD ROCK: Light gray with orange staining, moderately to slightly weathered, close fracturing, hard, BIOTITE QUARTZ GNEISS
266.6	46.7		3:12							266.6 (5 joints at 0-10°, tight with iron staining; 1 joint at 90°, tight with iron staining)
		5.0	2:26 3:20 3:55 4:19 4:47	(5.0) 100%	(4.7) 94%	RUN 2	(154.2) 99%	(148.9) 96%		HARD ROCK: Light gray, with trace pink and white, locally with orange staining, very slightly weathered to fresh, close to wide fracturing, hard to very hard, BIOTITE QUARTZ GNEISS with trace magnetite
261.6	51.7	5.0	5:14 4:24 6:52 5:26 6:57	(5.0) 100%	(4.1) 82%	RUN 3				(1 joint at 0°, tight; 2 joints at 60°, tight with trace iron staining; 1 joint at 90°, tight with iron staining)
256.6	56.7	5.0	8:22 8:20 10:41 12:33 15:37	(5.0) 100%	(5.0) 100%	RUN 4 RS-6				(2 joints at 10°, tight with trace iron staining; 1 joint at 30°, tight with trace iron staining; 1 joint at 90°, tight with iron staining)
251.6	61.7	5.0								(1 joint at 10°, tight with trace mica)
250.3	63.0	1.3	6:48/0.2 3:09/0.1 6:24/0.5 4:15/0.2 6:41/0.3	(1.3) 100%	(0.0) 0%	RUN 5 RUN 6 RUN 7 RUN 8 RUN 9				Note: RUN 5 to RUN 9 shown together due to short run lengths. Inner core barrel blocking off due to standard size HQ bit installed after RUN 4 completed (mistaken for HQ3 sized bit). Proper sized HQ3 core bit installed after RUN 9 completed.
246.6	66.7	3.7	11:14/0.7 14:29 26:32 31:04	(3.7) 100%	(3.3) 89%	RUN 10 RUN 11				(2 joints at 10°, tight with iron staining; 1 joint at 30°, tight)
241.6	71.7	5.0	6:48 4:28 4:22 4:40 2:58	(5.0) 100%	(4.8) 96%					(3 joints at 30°, tight with trace iron staining)
236.6	76.7	5.0	2:34 2:46 3:11 3:48 2:43	(5.0) 100%	(4.9) 98%	RUN 12				(1 joint at 0°, tight with iron staining)
231.6	81.7	5.0	3:42 3:45 4:58 4:37 4:55	(5.0) 100%	(5.0) 100%	RUN 13				(Coarse grained/pegmatitic zone from 83.4 to 83.7 ft)
227.5	85.8	4.1	6:48 10:34 12:19 21:09	(4.1) 100%	(4.1) 100%	RUN 14				
226.6	86.7	0.9	5:58/0.1	(0.8) 89%	(0.8) 89%	RUN 15				
225.2	88.1	1.4	5:25/0.9	(1.4) 100%	(1.4) 100%	RUN 16				(0.1 ft thick quartz vein at 40°)
221.6	91.7	3.6	12:50 12:34/0.4 8:05/0.6	(3.6) 100%	(3.6) 100%	RUN 17				(Mechanical fractures)
216.6	96.7	5.0	4:12 4:31 5:35 2:21 2:35 2:05 1:58 2:35	(5.0) 100%	(5.0) 100%	RUN 18 RS-7				(Mechanical fractures)
211.6	101.7	5.0	2:05 2:58 2:32 2:31 2:29	(5.0) 100%	(5.0) 100%	RUN 19				(Pegmatitic quartz + feldspar vein from 96.9-97.3 feet)
206.6	106.7	5.0	2:10 2:25 2:31 2:42 3:10	(5.0) 100%	(5.0) 100%	RUN 20				(No Joints)
201.6	111.7	5.0	2:56 2:07 2:54 1:38 1:52	(5.0) 100%	(5.0) 100%	RUN 21				(No Joints)
196.6	116.7	5.0	2:06 2:13 2:32 2:55 2:09 2:27 2:28	(5.0) 100%	(5.0) 100%	RUN 22				(1 joint at 0°, tight with trace staining; pegmatitic quartz + feldspar vein from 115.0-115.3 feet)
		5.0		(4.9) (4.9)		RUN 23				(1 joint at 25°, tight)

NORTH ANNA 3 CORE NORTH ANNA 3 PROJECT.GPJ NORTH ANNA 3.GDT 12/4/09



SHEET 2 OF 3

BECHTEL PROJECT NO.: 25161	MACTEC PROJECT NO.: 6468-09-2473	COUNTY: Louisa, VA	GEOLOGIST: R. Clark
SITE DESCRIPTION: North Anna 3 Project Supplement 2		DRILLER: T. Hahn/R. Hall	FLUID LEVEL (ft)
BORING NO.: M-30 (DH)	DRILL METHOD: Mud Rotary/Rock Core	DRILL MACHINE: CME-55 Track (RAL)	0 HR. NA
GROUND ELEV.: 313.3 ft (NAVD88)	NORTHING: 3,909,695 US ft (NAD83)	EASTING: 11,685,382 US ft (NAD83)	24 HR. 25.4
TOTAL DEPTH: 201.7 ft	SAMPLE METHODS: ASTM D 1586-08a; 2488-09a; 2113-08; 6032-08		HAMMER (ID): 140-lb. Auto (MEC-21)
DATE STARTED: 9/1/09	COMPLETED: 9/9/09	CASING DEPTH: 42.2 ft	CORE BARREL TYPE: Wireline HQ3 Triple Tube, series 6 & 10 bits

ELEV. (ft)	DEPTH (ft)	RUN (ft)	DRILL RATE (Min/ft)	RUN		SAMP. NO.	STRATA		L O G	DESCRIPTION AND REMARKS
				REC. (ft) %	RQD (ft) %		REC. (ft) %	RQD (ft) %		
										Continued from previous page
191.6	121.7		2:35 2:28 2:55	98%	98%					HARD ROCK: Light gray, with trace pink and white, locally with orange staining, very slightly weathered to fresh, close to wide fracturing, hard to very hard, BIOTITE QUARTZ GNEISS with trace magnetite (<i>continued</i>) (3 joints at 30°, tight to open with iron staining, moderately weathered zone from 123.7-124.9 ft)
		5.0	2:04 3:08 1:19 2:27 1:54	(5.0) 100%	(4.2) 84%	RUN 24				
186.6	126.7	5.0	2:28 2:38 2:26 2:38 2:45	(5.0) 100%	(5.0) 100%	RUN 25				(No Joints)
181.6	131.7	5.0	2:38 2:49 3:13 3:13 3:05	(5.0) 100%	(5.0) 100%	RUN 26				(Mechanical Fractures)
176.6	136.7	5.0	3:06 3:22 3:46 4:37 5:01	(5.0) 100%	(5.0) 100%	RUN 27				(1 joint at 45°, tight with trace iron staining; 1 joint at 60°, tight)
171.6	141.7	5.0	7:27 8:37 1:46 2:33 1:42	(4.9) 98%	(4.9) 98%	RUN 28				(1 joint at 75°, tight with trace iron staining)
166.6	146.7	5.0	2:22 2:43 2:45 2:58 2:32	(5.0) 100%	(5.0) 100%	RUN 29				(1 joint at 45°, tight)
161.6	151.7	5.0	3:18 3:12 4:10 5:25 4:41	(5.0) 100%	(4.5) 90%	RUN 30				(2 joints at 80-90°, tight)
156.6	156.7	4.0	2:26 2:38 3:43 5:30	(4.0) 100%	(3.2) 80%	RUN 31				(1 joint at 10°, tight with trace iron staining; 1 joint at 45°, tight)
152.6	160.7		4:08	(0.6)	(0.6)	RUN 32				(No Joints)
151.6	161.7	1.0	2:57 3:29 3:07 3:29 1:58	60%	60%	RUN 33				(1 joint at 35°, tight)
146.6	166.7	5.0	2:48 3:18 3:05 2:59 3:28	(5.0) 100%	(4.9) 98%	RUN 34 RS-9				(3 joints at 50°, tight)
141.6	171.7	5.0	2:56 3:22 3:43 4:25 5:13	(5.0) 100%	(5.0) 100%	RUN 35				(No joints; foliation at 45°)
136.6	176.7	5.0	7:22 5:59 6:29 8:07 3:21	(5.0) 100%	(5.0) 100%	RUN 36				(No Joints)
131.6	181.7	5.0	3:08 2:59 3:20 3:34 3:45	(5.0) 100%	(5.0) 100%	RUN 37				(1 joint at 45°, tight with iron staining)
126.6	186.7	5.0	4:01 4:22 4:33 4:46 5:21	(5.0) 100%	(5.0) 100%	RUN 38				(1 joint at 45°, tight with trace iron staining)
121.6	191.7	5.0	4:49	(5.0)	(5.0)	RUN 39				(No Joints)

NORTH ANNA 3 CORE NORTH ANNA 3 PROJECT.GPJ NORTH ANNA 3.GDT 12/4/09




SHEET 3 OF 3

BECHTEL PROJECT NO.: 25161	MACTEC PROJECT NO.: 6468-09-2473	COUNTY: Louisa, VA	GEOLOGIST: R. Clark
SITE DESCRIPTION: North Anna 3 Project Supplement 2		DRILLER: T. Hahn/R. Hall	FLUID LEVEL (ft)
BORING NO.: M-30 (DH)	DRILL METHOD: Mud Rotary/Rock Core	DRILL MACHINE: CME-55 Track (RAL)	0 HR. NA
GROUND ELEV.: 313.3 ft (NAVD88)	NORTHING: 3,909,695 US ft (NAD83)	EASTING: 11,685,382 US ft (NAD83)	24 HR. 25.4
TOTAL DEPTH: 201.7 ft	SAMPLE METHODS: ASTM D 1586-08a; 2488-09a; 2113-08; 6032-08		HAMMER (ID): 140-lb. Auto (MEC-21)
DATE STARTED: 9/1/09	COMPLETED: 9/9/09	CASING DEPTH: 42.2 ft	CORE BARREL TYPE: Wireline HQ3 Triple Tube, series 6 & 10 bits

ELEV. (ft)	DEPTH (ft)	RUN (ft)	DRILL RATE (Min/ft)	RUN		SAMP. NO.	STRATA		L O G	DESCRIPTION AND REMARKS
				REC. (ft) %	RQD (ft) %		REC. (ft) %	RQD (ft) %		
										Continued from previous page
116.6	196.7	5.0	4:52 3:05 3:08 3:28	100%	100%					HARD ROCK: Light gray, with trace pink and white, locally with orange staining, very slightly weathered to fresh, close to wide fracturing, hard to very hard, BIOTITE QUARTZ GNEISS with trace magnetite (<i>continued</i>) (No Joints)
			3:35 2:28 2:36 3:42 3:25	(5.0) 100%	(5.0) 100%	RUN 40 RS-10				
111.6	201.7									
										111.6 201.7
										Boring and coring terminated at 201.7 feet.
										Boring closed by tremie method with cement-bentonite grout.
										24 hour water level measured on 9/09/2009 prior to drilling. Borehole was at a depth of 171.5 feet.


NORTH ANNA 3 CORE NORTH ANNA 3 PROJECT.GPJ NORTH ANNA 3.GDT 12/4/09

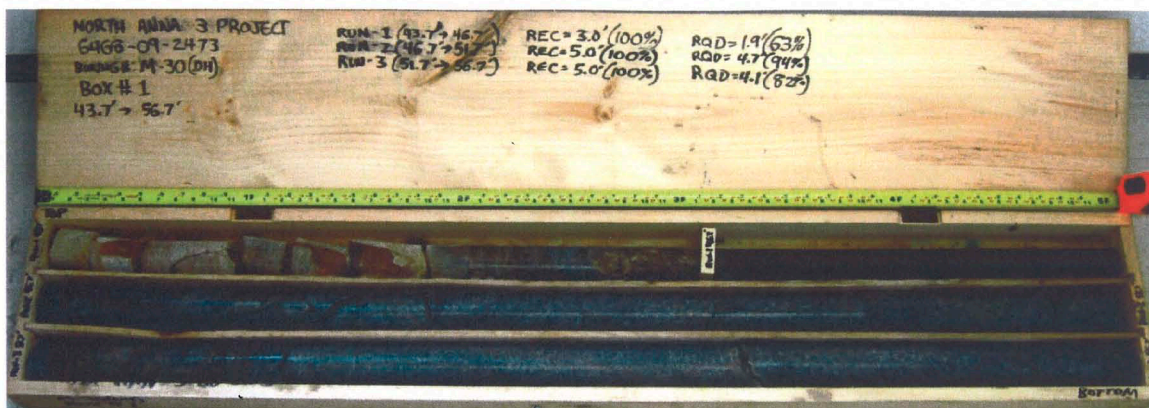


M-30(DH) – Box 1




M-30(DH) – Box 2

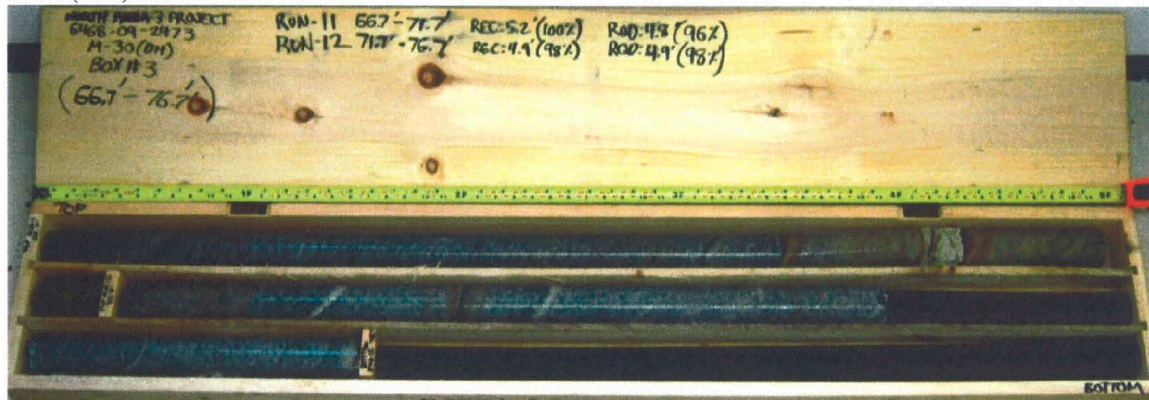


M-30(DH) – Box 3

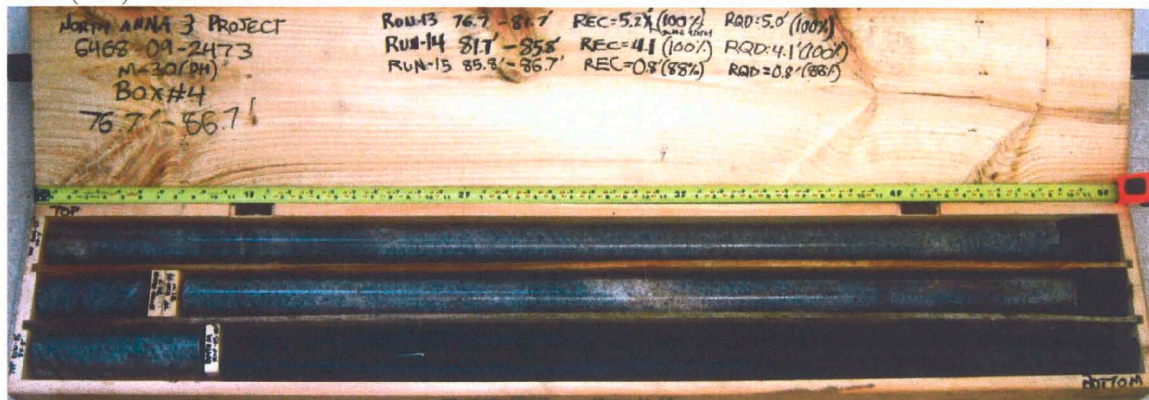


M-30(DH) – Box 4

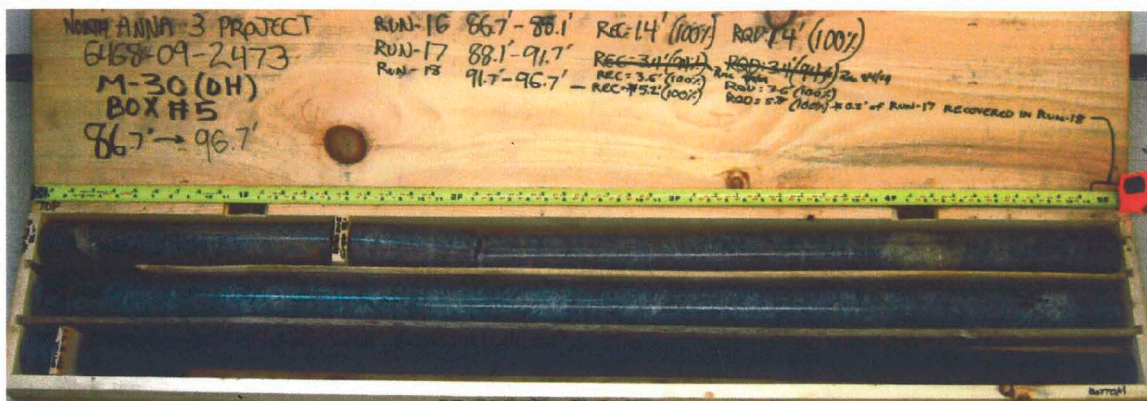


M-30(DH) – Box 5

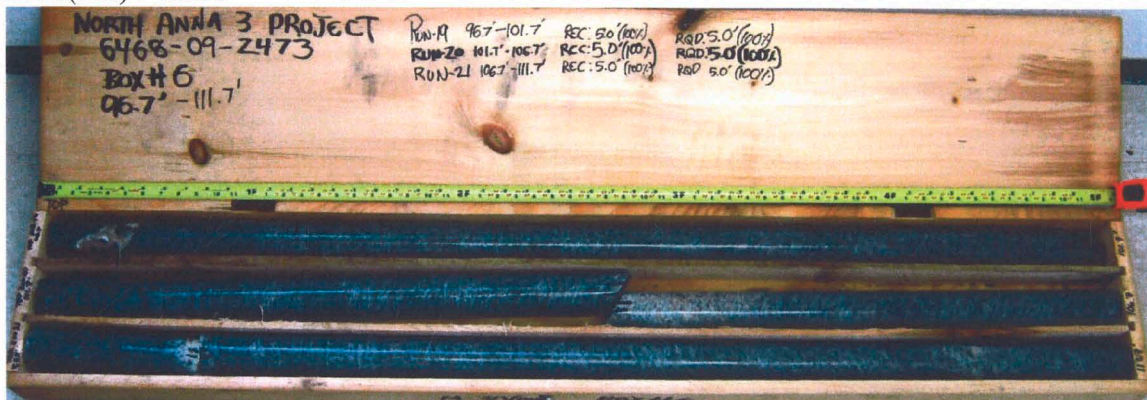


M-30(DH) – Box 6

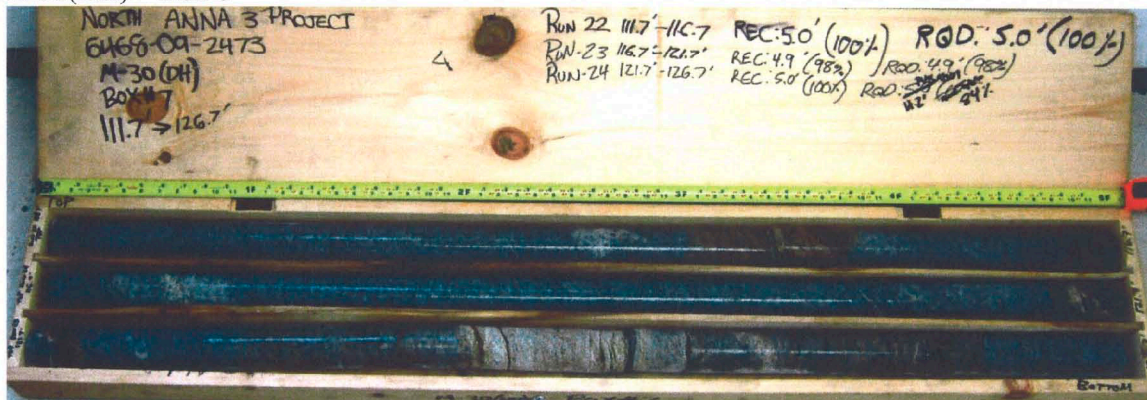


M-30(DH) – Box 7

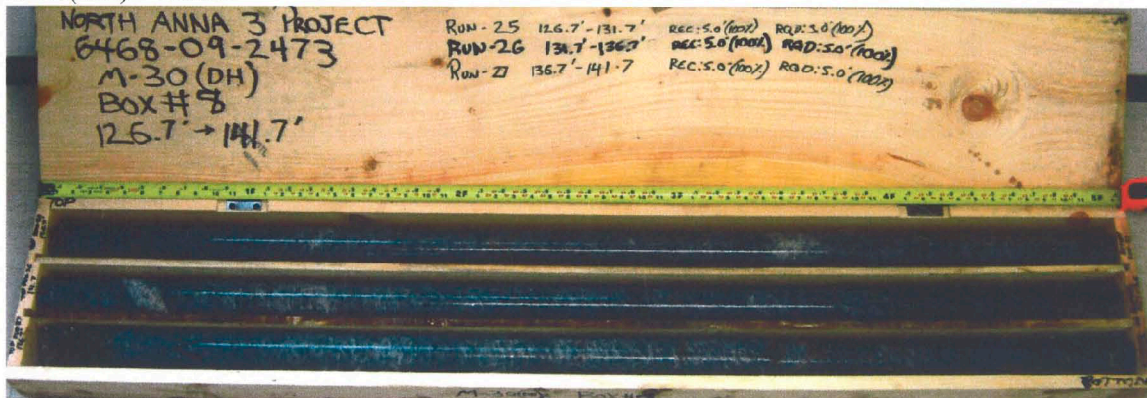


M-30(DH) – Box 8

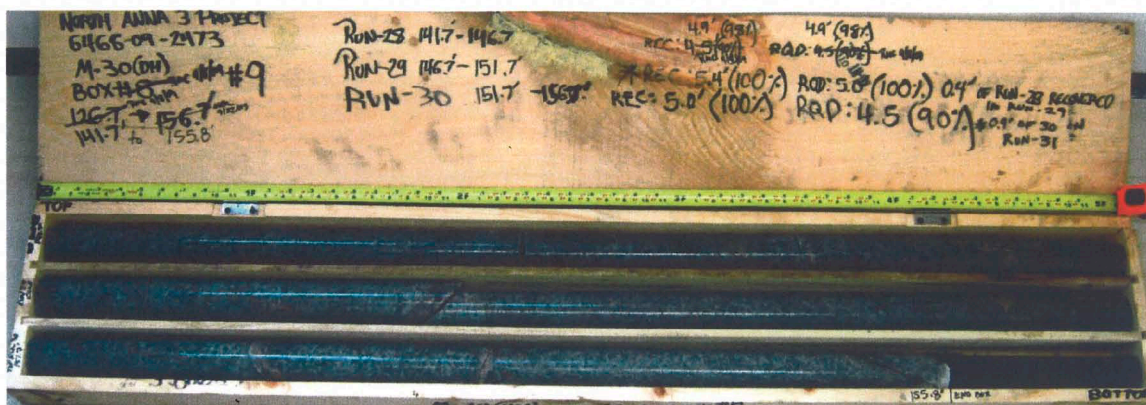


M-30(DH) - Box 9

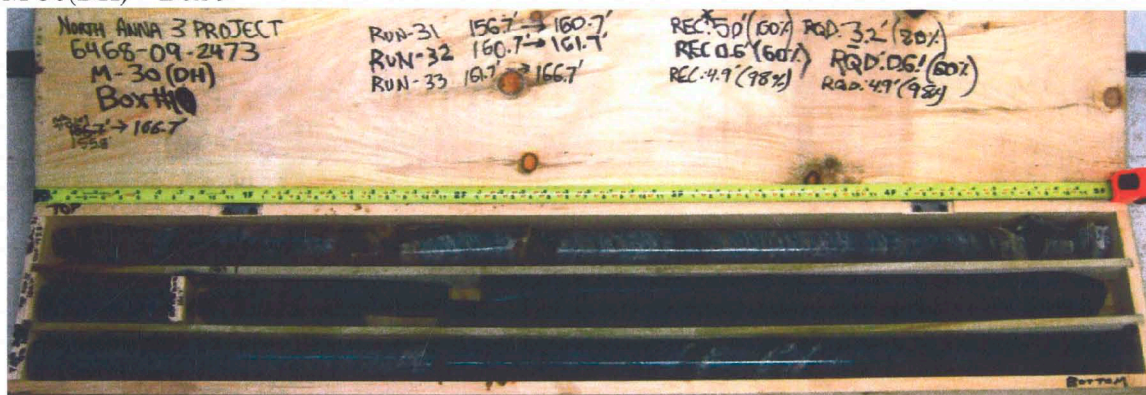

M-30(DH) - Box 10

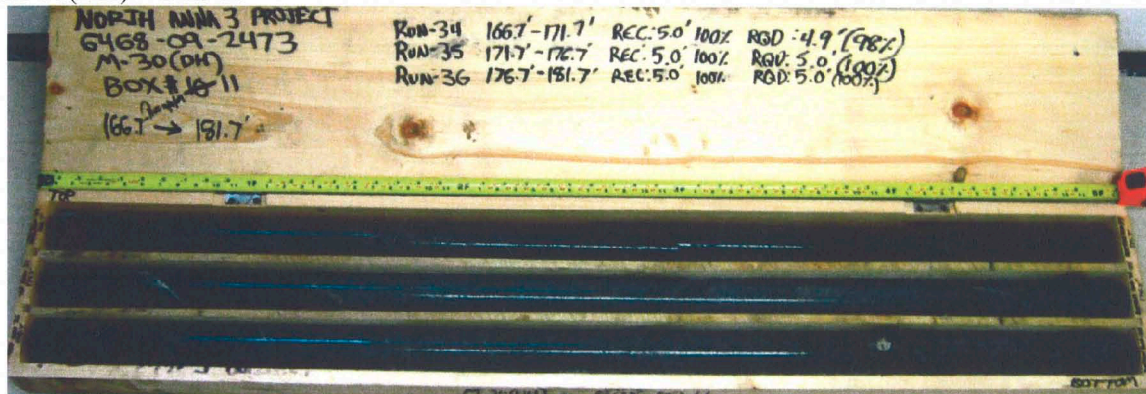

M-30(DH) - Box 11

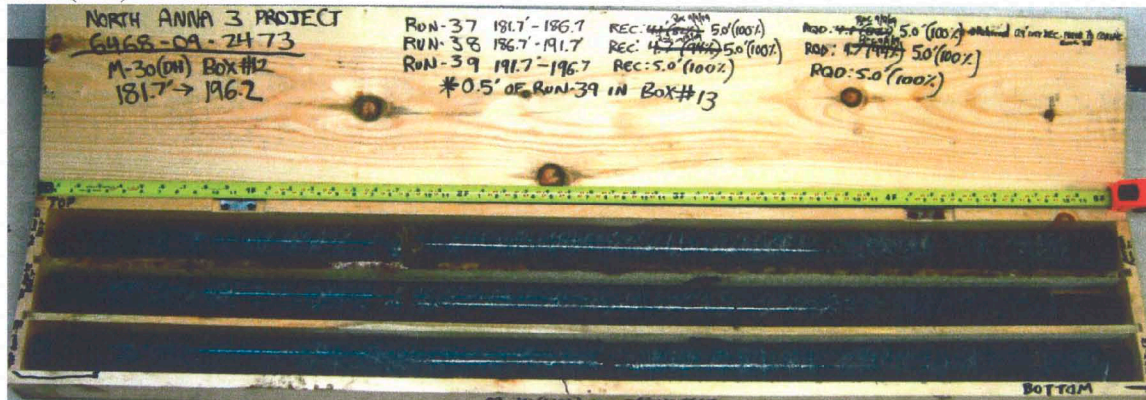

M-30(DH) - Box 12



M-30(DH) - Box 13
