

GENERIC LTP REVIEW SCHEDULE

GENERIC LTP REVIEW SCHEDULE

Thu 06/21/01

ID	Task Name	Duration	Start	Finish	2000				2001		
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3
1	License Termination Plan (LTP) Review	382 d	Fri 02/11/00	Mon 07/30/01							
2	Acceptance Review	101 d	Fri 02/11/00	Fri 06/30/00							
3	Receive LTP	0 d	Fri 02/11/00	Fri 02/11/00							
4	Forward to DCB	2 d	Fri 02/11/00	Mon 02/14/00							
5	Conduct Review	90 d	Tue 02/15/00	Mon 06/19/00							
6	Draft Memo to NRR	2 d	Tue 06/20/00	Wed 06/21/00							
7	Concurrence	3 d	Thu 06/22/00	Mon 06/26/00							
8	Issue Memo to NRR	1 d	Tue 06/27/00	Tue 06/27/00							
9	Issue to Licensee	3 d	Wed 06/28/00	Fri 06/30/00							
10	Develop SOW for PA & EA Contracto	25 d	Thu 06/22/00	Wed 07/26/00							
11	Technical Review	243 d	Thu 07/27/00	Mon 07/02/01							
12	Develop Task Plan	17 d	Thu 07/27/00	Fri 08/18/00							
13	Prepare Task Plan	7 d	Thu 07/27/00	Fri 08/04/00							
14	Review Task Plan	2 d	Mon 08/07/00	Tue 08/08/00							
15	Brief BC	1 d	Wed 08/09/00	Wed 08/09/00							
16	Revise Task Plan	2 d	Thu 08/10/00	Fri 08/11/00							
17	Approve Task Plan	1 d	Mon 08/14/00	Mon 08/14/00							
18	Prepare TAR(s)	1 d	Tue 08/15/00	Tue 08/15/00							
19	Prepare RFTA	1 d	Tue 08/15/00	Tue 08/15/00							
20	Forward RFTA	1 d	Wed 08/16/00	Wed 08/16/00							
21	Issue TAR(s)	3 d	Wed 08/16/00	Fri 08/18/00							


Project: ltp-gen
Date: Thu 06/21/01

Task

Critical Task

Progress

Milestone



Summary

Rolled Up Task

Rolled Up Critical Task

Rolled Up Milestone



Rolled Up Progress

Split

External Tasks

Project Summary



GENERIC LTP REVIEW SCHEDULE

Thu 06/21/01

ID	Task Name	Duration	Start	Finish	2000				2001		
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3
22	Evaluate LTP	43 d	Mon 08/21/00	Wed 10/18/00							
23	Characterization	15 d	Mon 08/21/00	Fri 09/08/00							
24	Dismantlement Activities	10 d	Mon 08/21/00	Fri 09/01/00							
25	Remediation Plans	5 d	Mon 08/21/00	Fri 08/25/00							
26	Final Radiation Survey Plan	25 d	Mon 09/11/00	Fri 10/13/00							
27	Compliance w/LTR	25 d	Mon 09/11/00	Fri 10/13/00							
28	Costs	10 d	Mon 09/04/00	Fri 09/15/00							
29	Supplement to ER	10 d	Mon 09/04/00	Fri 09/15/00							
30	Change Procedure	5 d	Mon 08/21/00	Fri 08/25/00							
31	Assemble Comments	3 d	Mon 10/16/00	Wed 10/18/00							
32	Hold Public Meeting	28 d	Tue 09/05/00	Thu 10/12/00							
33	Plan Meeting	4 w	Tue 09/05/00	Mon 10/02/00							
34	Prepare Briefing Materials	3 d	Tue 09/12/00	Thu 09/14/00							
35	Prepare Handouts	1 d	Tue 09/12/00	Tue 09/12/00							
36	Hold Dry Run	1 d	Fri 09/15/00	Fri 09/15/00							
37	Revise Materials/Handouts	2 d	Mon 09/18/00	Tue 09/19/00							
38	Conduct Meeting	3 d	Tue 10/03/00	Thu 10/05/00							
39	Analyze Comments	5 d	Fri 10/06/00	Thu 10/12/00							
40	Develop RAI (first)	26 d	Thu 10/19/00	Thu 11/23/00							
41	Prepare Draft SER	10 d	Thu 10/19/00	Wed 11/01/00							
42	Develop Draft RAI	5 d	Thu 11/02/00	Wed 11/08/00							


Project: ltp-gen
Date: Thu 06/21/01

Task

Critical Task

Progress

Milestone




Summary

Rolled Up Task

Rolled Up Critical Task

Rolled Up Milestone



Rolled Up Progress

Split


External Tasks

Project Summary



GENERIC LTP REVIEW SCHEDULE

Thu 06/21/01

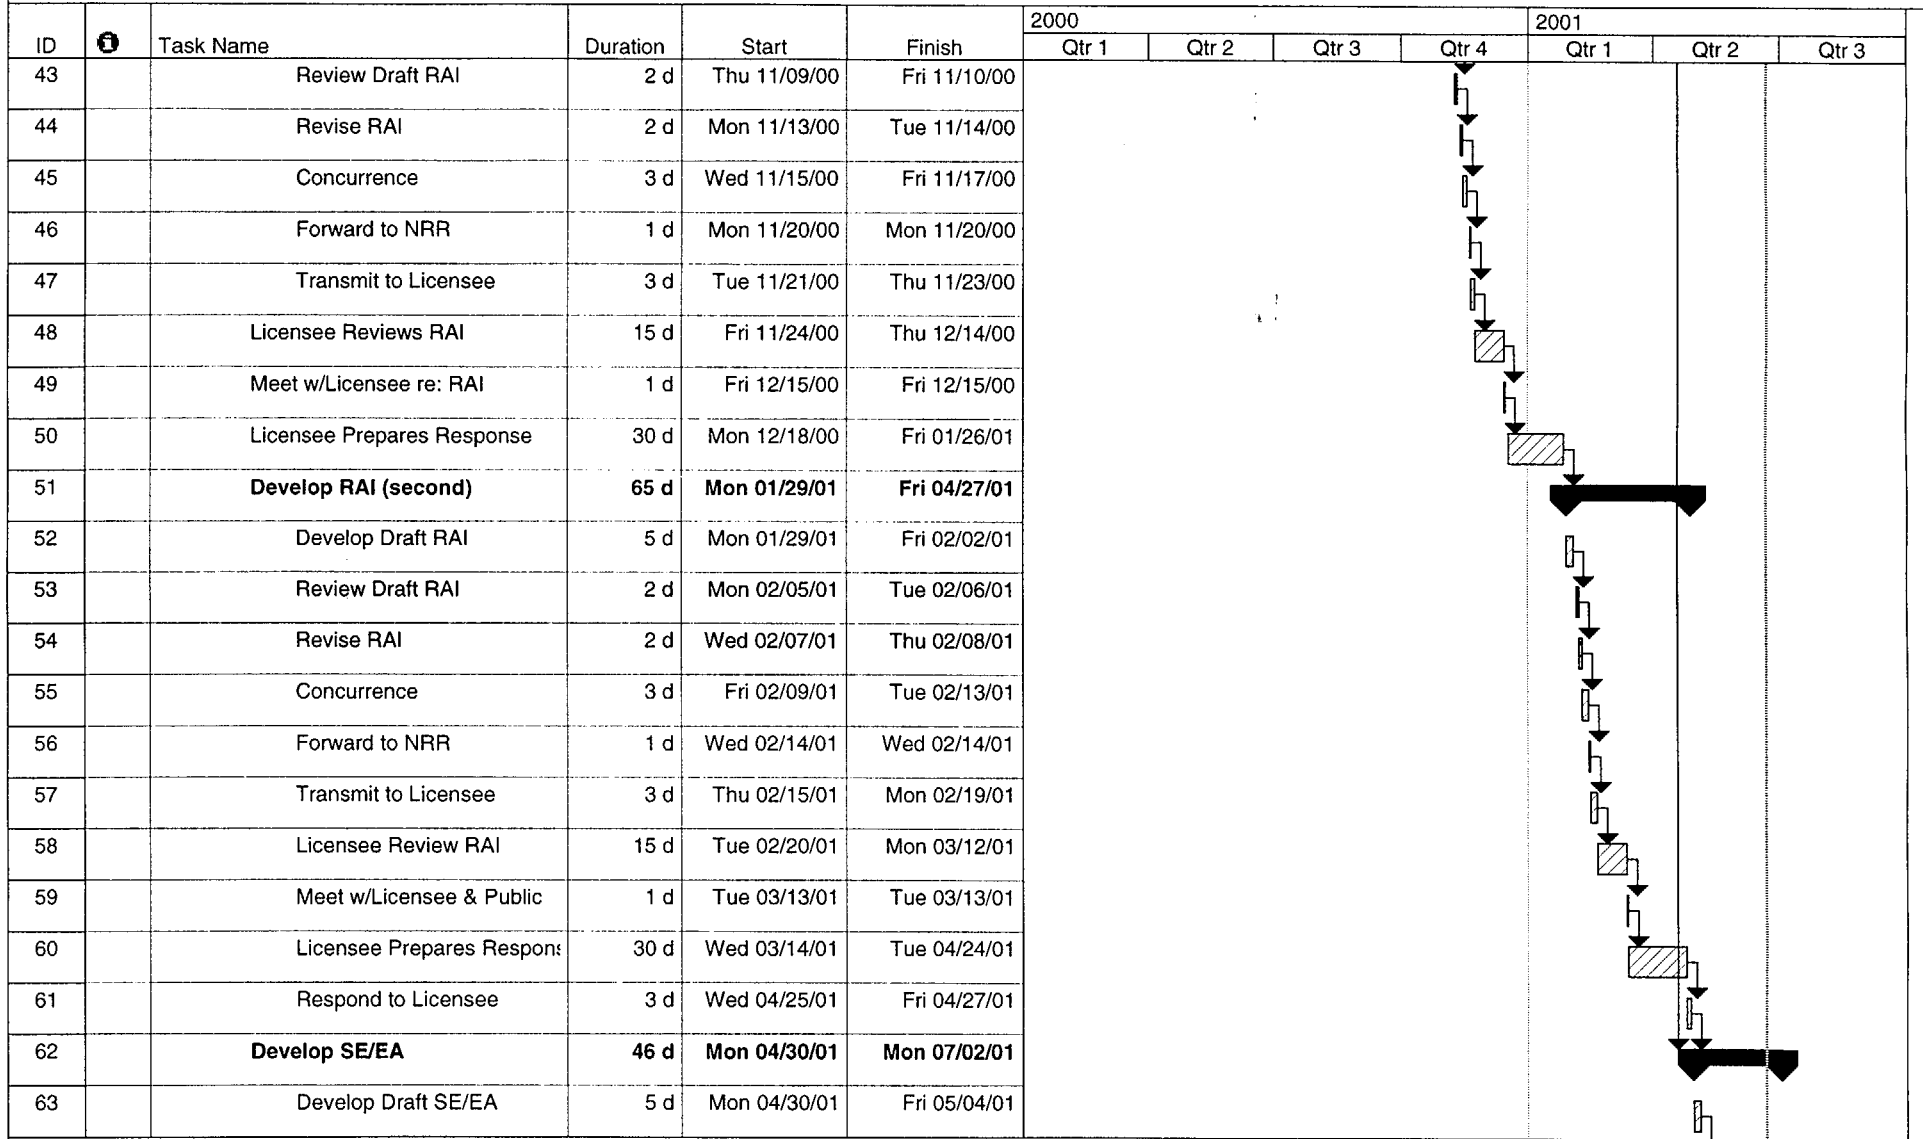

Project: ltp-gen
Date: Thu 06/21/01

Task

Critical Task

Progress

Milestone




Summary

Rolled Up Task

Rolled Up Critical Task

Rolled Up Milestone



Rolled Up Progress

Split

External Tasks


Project Summary



GENERIC LTP REVIEW SCHEDULE

Thu 06/21/01

ID	Task Name	Duration	Start	Finish	2000				2001		
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3
64	Review SEEA (EIS/EA Tear	5 d	Mon 05/07/01	Fri 05/11/01							
65	Revise SE/EA	1 d	Mon 05/14/01	Mon 05/14/01							
66	Concurrence	2 w	Tue 05/15/01	Mon 05/28/01							
67	Review by State	22 d	Tue 05/29/01	Wed 06/27/01							
68	Revise SE/EA	3 d	Thu 06/28/01	Mon 07/02/01							
69	Complete LTP Review (NMSS)	20 d	Tue 07/03/01	Mon 07/30/01							
70	Finalize SER/EA/FONSI	7 d	Tue 07/03/01	Wed 07/11/01							
71	Review SER/EA/FONSI	2 d	Thu 07/12/01	Fri 07/13/01							
72	Concurrence	2 w	Mon 07/16/01	Fri 07/27/01							
73	Transmit SER/EA/FONSI to NR	1 d	Mon 07/30/01	Mon 07/30/01							
74	Complete NMSS Review	0 d	Mon 07/30/01	Mon 07/30/01							



Project: ltp-gen Date: Thu 06/21/01	Task		Summary		Rolled Up Progress	
	Critical Task		Rolled Up Task		Split	
	Progress		Rolled Up Critical Task		External Tasks	
	Milestone		Rolled Up Milestone		Project Summary	
